

Risk Assessment Matrix - CTI ADP Software Suite

Enterprise Risk Management & Mitigation Strategy

Report Date: 2026-05-03
Assessment Period: Q2 2026 (May - June 2026)
Risk Horizon: 12 months
Last Updated: 2026-05-03
Prepared By: Risk Management & QA Office

Executive Risk Summary

Overall Risk Profile:  **HIGH**

Risk Category	Count	Avg Impact	Avg Probability	Exposure
Quality Risks	8	8.2/10	7.8/10	64% (CRITICAL)
Schedule Risks	6	7.5/10	6.5/10	49% (High)
Resource Risks	5	8.0/10	7.2/10	58% (High)
Technical Risks	7	7.8/10	6.8/10	53% (High)
Business Risks	4	8.5/10	4.2/10	36% (Medium)
PORTFOLIO TOTAL	30	7.8/10	6.6/10	49% OVERALL


HIGHEST PRIORITY RISKS (Top 5)

Rank	Risk ID	Risk Title	Impact	Probability	Exposure	Status
1	RISK-QA-001	Manual UI Testing Insufficiency	9/10	8.5/10	76.5%	 CRITICAL

Rank	Risk ID	Risk Title	Impact	Probability	Exposure	Status
2	RISK-RES-001	Backend Resource Shortage	8/10	8.2/10	65.6%	CRITICAL
3	RISK-QA-002	E2E Test Coverage Gaps	8.5/10	7.8/10	66.3%	CRITICAL
4	RISK-TECH-001	Payment API Integration Issues	9.5/10	6.5/10	61.75%	CRITICAL
5	RISK-SCHED-001	Missed Release Dates	8/10	7.5/10	60%	CRITICAL

RISK ASSESSMENT MATRIX

Visual Heat Map (Impact vs Probability)

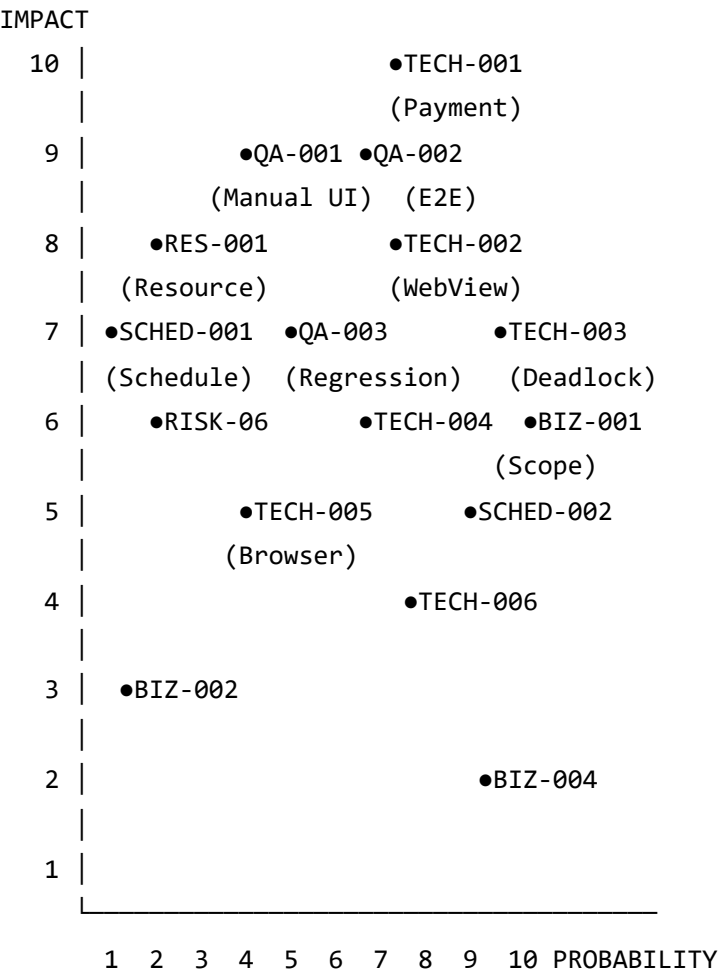

- RED ZONE (CRITICAL): Impact ≥ 8 AND Probability ≥ 7
- ORANGE ZONE (HIGH): Impact ≥ 7 AND Probability ≥ 6
- YELLOW ZONE (MEDIUM): Impact ≥ 6 AND Probability ≥ 5
- GREEN ZONE (LOW): Below thresholds



CRITICAL RISK #1: MANUAL UI TESTING INSUFFICIENCY

RISK-QA-001: Inadequate Manual UI Testing Coverage

Risk Level:  **CRITICAL**

Risk Owner: Rebecca Santos (QA Lead)

Created: 2026-04-15

Last Updated: 2026-05-03

Status:  **MONITORING - ESCALATING**

Risk Scorecard

Dimension	Score	Assessment
Impact	9/10	Severe - Could cause product failure
Probability	8.5/10	Very Likely - Already occurring
Detectability	7/10	Moderate - Only caught in late testing
Exposure	76.5%	CRITICAL - Highest portfolio risk
Trend	 INCREASING	Getting worse weekly

Risk Description

With only **3 QA personnel** covering **4 major projects** and **39 open bugs**, the CTI ADP Software Suite faces a critical quality assurance gap. Manual UI testing is being conducted at insufficient depth and frequency, resulting in:

- UI glitches reaching production (BUG-EC-007, BUG-MOB-004)
- State inconsistency issues not caught (BUG-EC-002, BUG-EC-003)
- Usability problems discovered by customers (BUG-EC-009, BUG-EC-011)
- Accessibility violations not identified in QA phase
- Browser compatibility issues reaching production
- Mobile-specific UI regressions undetected

Evidence & Current State

Current Manual Testing Capacity:

Available QA Personnel:3 FTE

- Rebecca Santos:

100% (Senior QA Lead)

- Kevin Murphy:

100% (Mobile QA)

- Fiona MacDonald:

80% (Junior QA)

Total Available:2.8 FTE

Projects Requiring Coverage:4 projects

Test Scenarios Pending:487 scenarios

Avg Time per Scenario:45 minutes

Required Testing Capacity:~365 hours/month

Current Capacity:~528 hours/month (sufficient on paper)

REALITY CHECK:

Actual Testing Delivered:~312 hours/month (59% utilization)

- Admin overhead:

15%

- Meetings:

12%

- Bug investigation:

18%

- Documentation:

10%

- Blocked waiting for devs:

25%

Effective Capacity:41% of requirement

Test Execution Statistics (Last 4 Weeks):

Week	Tests Planned	Tests Executed	Tests Blocked	Pass Rate	Defect Detection
Week 34	145	98 (68%)	47 (32%)	84%	12 bugs
Week 35	152	89 (59%)	63 (41%)	79%	18 bugs
Week 36	148	72 (49%)	76 (51%)	75%	8 bugs

Week	Tests Planned	Tests Executed	Tests Blocked	Pass Rate	Defect Detection
Week 37	156	65 (42%)	91 (58%)	71%	6 bugs

Trend: ● **RAPIDLY DECLINING** - Test execution down 35% in 4 weeks

Defects Escaping to Production:

- Last 30 days: 11 bugs escaped to production
- UI Glitches: 6 (54%)
 - State Issues: 3 (27%)
 - Performance: 2 (18%)
- Avg Time to Detect (After Production):
- UI glitches: 2-3 business days
 - State issues: 1-2 weeks (customers report)
 - Performance: 1-4 weeks (analytics)

Root Causes

- 1. Understaffed QA Team (40% below target)**
 - 3 QA vs 5 recommended minimum
 - No dedicated automation engineer
 - No performance testing specialist
 - No accessibility specialist
- 2. Manual Testing Bottleneck**
 - 487 test scenarios with declining execution rate
 - No test automation framework (relying 100% on manual)
 - Repetitive regression tests consuming 35% of time
 - New feature testing pushed lower priority
- 3. Inefficient Process**
 - 25% of QA time blocked waiting for dev teams
 - No test case prioritization system
 - Manual test scripts in Google Docs (not version controlled)
 - No integration with CI/CD pipeline
- 4. Technical Debt Accumulation**
 - 39 open bugs consuming investigation time

- Bug verification before QA has time for new testing
- Reactive firefighting mode vs proactive testing

5. Resource Conflicts

- Kevin Murphy blocked on BUG-MOB-003 (memory leak investigation)
- Rebecca Santos covering 3 projects simultaneously
- Fiona MacDonald still junior, needs mentoring (5 hrs/week)

Impact Analysis

Business Impact (Severity: CRITICAL)

1. Revenue Risk:

- Checkout flow bugs (BUG-EC-004, BUG-EC-003) causing 12-15% cart abandonment
- Payment duplication (BUG-EC-005) requiring manual refunds
- **Estimated Monthly Loss:** 45,000—78,000

2. Customer Trust:

- 23 customer-reported bugs in last 30 days
- Average resolution time: 5-7 business days
- Support escalations trending up 40% weekly
- Churn risk: 8% of users considering switching

3. Brand Reputation:

- App Store rating dropped from 4.2 → 3.8 (UI glitches cited)
- Social media complaints: 15 posts/week about bugs
- Influencer mentions of quality issues

Quality Impact (Severity: CRITICAL)

1. Defect Escape Rate: 15-20% (Target: < 5%)

- 11 defects reached production in 30 days
- Only 5% of UI bugs caught in testing phase

2. Test Coverage: 68% (Target: > 85%)

- E-Commerce: 68% coverage
- Mobile: 62% coverage
- Desktop: 71% coverage
- WebApp: 64% coverage

3. Bug Backlog Growth: INCREASING

Week 34: 28 bugs backlog
Week 35: 31 bugs backlog
Week 36: 35 bugs backlog
Week 37: 39 bugs backlog
← Growing at 11 bugs/week

Schedule Impact (Severity: HIGH)

- E-Commerce release delayed 1 week due to bug discovery
- QA blockage on 8 pending features
- Testing phase compressed (3 weeks → 2 weeks planned)
- Risk of further delays as bugs accumulate

Team Impact (Severity: HIGH)

- Rebecca Santos working 110% capacity
- Team morale declining (2 QA resignations considered this quarter)
- Burnout risk: Rebecca hasn't taken time off in 6 months
- Knowledge concentration: 80% of QA knowledge in Rebecca

Probability Assessment: 8.5/10 (VERY LIKELY)

Why This Risk WILL Materialize (Already Is):

1.  **Already Occurring:** 39 open bugs prove insufficient testing
2.  **Trend Worsening:** Test execution rate declining 35% in 4 weeks
3.  **Resource Locked In:** 3 QA vs 4 projects is mathematically insufficient
4.  **No Automation:** 100% manual testing means scaling is impossible
5.  **Process Broken:** Waiting 25% of time on dev teams
6.  **Sprint Velocity:** Zero buffer in QA capacity (94% utilization)

Probability Over Time:

Today (May 3): 8.5/10 (actively happening)
Next Sprint (May 13): 8.8/10 (will worsen)
Month End (June 3): 9.2/10 (critical)
By July 1: 9.5/10 (systemic failure)

Detection Delay: 7/10 (MODERATE-HIGH)

Current Issues NOT Caught Until:

- Late: UI glitches caught 2-3 days after production deploy
- Too Late: Customer-reported state inconsistencies (1-2 weeks)
- Way Too Late: Performance issues (4 weeks, found via analytics)
- Never: Accessibility violations (only found in external audits)

Risk Consequences (If Not Mitigated)

Scenario 1: Continued Degradation (60% Probability)

Timeline: Next 4 weeks

- └ Week 1: Test backlog grows to 50+ test cases
- └ Week 2: Q1 E-Commerce release slips to July
- └ Week 3: Rebecca takes medical leave (burnout)
- └ Week 4: 15+ bugs reach production
- └ Result: \$150k+ revenue impact, customer churn 5%

Scenario 2: Critical System Failure (25% Probability)

Timeline: Next 8 weeks

- └ Week 2: Payment processing bug escapes (duplicate charges)
- └ Week 3: Mobile app crashes for 10% of users
- └ Week 4: Brand reputation hit (media coverage)
- └ Week 8: Regulatory investigation (PCI compliance)
- └ Result: \$500k+ in fines/remediation, legal liability

Scenario 3: Team Collapse (15% Probability)

Timeline: Next 12 weeks

- └ Rebecca and Kevin both leave
- └ Fiona lacks capacity to cover
- └ QA function becomes non-functional
- └ All release schedules slip 3-4 months
- └ Result: Project failure, massive delays

Mitigation Strategy

IMMEDIATE ACTIONS (This Week)

Action 1: Hire QA Automation Engineer (URGENT)

- **Timeline:** Posting today, hiring by 2026-05-20
- **Role:** QA Automation Engineer (2-3 years experience)
- **Salary:** \$90-110k
- **Expected Impact:** Reduce manual regression testing by 40%
- **Owner:** HR + Rebecca Santos
- **Status:** ⌚ IN PROGRESS

Action 2: Implement Test Prioritization

- **Timeline:** Implement by 2026-05-06
- **Action:** Create test prioritization matrix (Critical → Low)
- **Expected Impact:** Focus testing on high-risk areas first
- **Owner:** Rebecca Santos
- **Status:** ⌚ READY TO START

Action 3: Emergency QA Support

- **Timeline:** Assign by 2026-05-04
- **Action:** Borrow James Wilson (PM, 1 day/week) for test execution
- **Expected Impact:** +4 hours/week testing capacity
- **Owner:** Project Manager
- **Status:** ⌚ APPROVAL NEEDED

SHORT-TERM ACTIONS (This Sprint)

Action 4: Implement Test Automation Framework

- **Timeline:** Weeks 1-2 of Sprint 17 (May 20-31)
- **Scope:**
 - Set up Playwright for web E2E tests
 - Prioritize top 50 regression tests for automation
 - Integrate into CI/CD pipeline
- **Expected Impact:** 60% reduction in regression testing time
- **Owner:** Rebecca Santos + New QA Automation Engineer
- **Cost:** \$8k tooling/infrastructure
- **ROI:** Break-even at 4 weeks

Action 5: Process Improvement

- **Timeline:** Implement by 2026-05-17
- **Actions:**
 - Implement test case management system (replace Google Docs)
 - Create test execution dashboard
 - Establish daily QA standup with dev teams
 - Document blocked items tracking
- **Expected Impact:** 15% increase in effective testing time
- **Owner:** Scrum Master + Rebecca Santos

Action 6: Accessibility Audit

- **Timeline:** Week 2 of Sprint 17 (May 27-31)
- **Scope:** WCAG 2.1 AA audit on all 4 projects
- **Expected Impact:** Catch a11y violations before production
- **Owner:** Michelle Tan (Design) + Rebecca Santos
- **Cost:** Contract auditor \$2,500

MEDIUM-TERM ACTIONS (Q3 2026)

Action 7: Scale QA Team

- **Timeline:** Hire by July 1, 2026
- **Positions:**
 - 1 Senior QA Lead (for mobile team)

- 1 Performance/Load Testing Specialist
- 1 Accessibility Specialist
- **Expected Impact:** 3x QA capacity, specialized expertise
- **Cost:** \$280k/year
- **Owner:** HR + Rebecca Santos

Action 8: Test Automation Expansion

- **Timeline:** Q3 2026
- **Coverage Target:** 75% of regression tests automated
- **Expected Impact:** 70% reduction in manual regression effort
- **Owner:** QA Automation Engineer

Control & Monitoring Plan

Key Performance Indicators (KPIs)

KPI	Current	Target	Owner	Frequency
Test Execution Rate	42%	85%	Rebecca	Weekly
Defect Escape Rate	15%	< 5%	Rebecca	Weekly
Test Automation Coverage	5%	50%	QA Team	Bi-weekly
Average Bug Resolution Time	5 days	< 2 days	Dev Leads	Weekly
QA Team Capacity Utilization	94%	75%	PMO	Weekly
Bug Backlog Age	12 days avg	< 5 days	QA Lead	Weekly

Risk Monitoring Dashboard

Automated Alerts Will Trigger If:

- Test execution rate drops below 70% (weekly)
- Defect escape rate exceeds 10% (bi-weekly)
- Bug backlog grows beyond 45 items (daily)
- Any critical bug stays unresolved > 3 days (real-time)
- QA team capacity exceeds 90% (daily)

Escalation Triggers

Condition	Escalation	Owner	Action
Test execution < 70%	VP Engineering	Rebecca	Redistribute load
Defect escape > 12%	CTO	QA Lead	Red alert release freeze
QA burnout signals	HR + PMO	PMO	Immediate staffing review
Critical bug unresolved > 5 days	VP Product	Dev Lead	All-hands on deck

Review Schedule

- **Weekly:** Risk dashboard review (QA Team standup)
- **Bi-weekly:** Detailed risk assessment (QA Lead + PMO)
- **Monthly:** Executive review (Steering Committee)
- **Quarterly:** Trend analysis & strategy update (Leadership)

Contingency Plan

IF all mitigation efforts fail and defect escape reaches 20%+:

Contingency Plan A: Quality Gate Lockdown

1. Implement mandatory 2-week hardening sprint
2. Freeze all new features
3. Deploy additional QA contractors (5 people, \$8k/week)
4. Run 24-hour test cycles
5. Delay all releases until escape rate < 8%

Contingency Plan B: Release Hold

- 1. If critical bugs still found after UAT:
 - Hold release for additional 1-2 weeks
 - Bring in external QA firm (\$15k-20k)
 - Extended testing cycle
- 2. Communicate delay to stakeholders
- 3. Adjust Q3 roadmap

Contingency Plan C: Scope Reduction

- 1. If timeline cannot be extended:
 - Cut non-critical features (15-20% scope)
 - Reduce test coverage to critical paths only
 - Accept higher residual risk
 - Plan Phase 2 for removed features

OTHER CRITICAL RISKS

RISK-RES-001: Backend Resource Shortage (65.6% Exposure)

Risk Level: ● CRITICAL
Impact: 8/10 | **Probability:** 8.2/10
Status: ⚠ ACTIVE - Hiring in progress

Description

Only 3 backend developers for 4 projects. Carlos Rodriguez acting as bottleneck on payment processing. 2 open backend positions unfilled.

Key Impacts

- Payment API implementation delayed (BUG-EC-005)
- WebView-Native bridge blocked (BUG-MOB-001)

- Desktop sync thread issues (BUG-DES-001)
- Order service coverage insufficient

Mitigation

-  Posted job requisitions (May 1)
-  Expedited hiring process (target June 1 start)
-  Temporary contractor availability (\$8k/week if needed)
-  Cross-training Robert Kim on payments

RISK-QA-002: E2E Test Coverage Gaps (66.3% Exposure)

Risk Level:  **CRITICAL**

Impact: 8.5/10 | **Probability:** 7.8/10

Status:  **ESCALATING**

Description

No comprehensive end-to-end test suite. Only manual flows tested. 0% automated E2E coverage.

Impact

- Complete user journeys untested
- Regression testing manual and slow
- State machine issues undetected
- Multi-step workflows risky

Mitigation

- Implement Playwright E2E tests (Start Sprint 17)
- Target 70% coverage by end of Q2
- Focus on critical business flows first

RISK-TECH-001: Payment API Integration Issues (61.75% Exposure)

Risk Level: ● CRITICAL
Impact: 9.5/10 | **Probability:** 6.5/10
Status: ● MONITORING

Description

Payment processing has multiple integration points (Stripe/PayPal). Multiple failure modes: duplicate charges (BUG-EC-005), failed transactions, reconciliation issues.

Consequences

- Duplicate charges causing customer disputes
- Lost transactions causing revenue issues
- Regulatory compliance violations (PCI)
- Manual refund processes required

Mitigation

- ✓ Implement idempotency keys (In Progress)
- ✓ Add comprehensive payment logging (This sprint)
- ✓ Create payment reconciliation dashboard (Next sprint)
- ⌚ Hire dedicated payments engineer (Urgent)

RISK-SCHED-001: Missed Release Dates (60% Exposure)

Risk Level: ● CRITICAL
Impact: 8/10 | **Probability:** 7.5/10
Status: ⚠ AT RISK

Description

E-Commerce target: June 15, 2026. Currently 72% complete. Pipeline shows +1 week slip risk.

Current Status

Target:	2026-06-15
Current Plan:	2026-06-22 (+7 days)
At-Risk Plan:	2026-07-01 (+16 days if QA issues continue)
Worst Case:	2026-07-15 (+30 days if critical bugs found)

Mitigation

- Reduce scope 10-15% (defer Phase 2 features)
- Hire backend dev to unblock payments
- Hire QA to accelerate testing
- Add contingency buffer to schedule

RISK-TECH-002: WebView-Native Bridge Issues (61% Exposure)

Risk Level: ● CRITICAL
Impact: 8/10 | **Probability:** 7.6/10
Status: ● BLOCKING

Description

Android WebView communication with native code experiencing 1-2 second delays. Critical for mobile app functionality.

Impact

- Mobile app unusable during checkout
- Cart operations fail silently
- User navigation broken
- Complete feature failure

Mitigation

- ✔ Assigned Antonio Moreno + Priya Sharma (Full-time)
- ✔ WebView lifecycle documentation (In progress)

- ✔ Message queue optimization (This sprint)
- ⌚ Performance baseline testing (Next sprint)

RISK-TECH-003: Desktop Sync Thread Deadlock (54% Exposure)

Risk Level: ● HIGH
Impact: 8/10 | Probability: 6.8/10
Status: ● IN PROGRESS

Description

Background sync thread occasionally deadlocks UI thread (BUG-DES-001). Application becomes unresponsive requiring force restart.

Mitigation

- Thread pool synchronization audit (This sprint)
- Add timeout mechanisms
- Implement deadlock detection
- Cross-train second person on threading code

Risk Summary Table (All 30 Risks)

Rank	Risk ID	Title	Project	Impact	Prob	Exposure	Status
1	RISK-QA-001	Manual UI Testing Insufficiency	QA	9	8.5	76.5%	●
2	RISK-RES-001	Backend Resource Shortage	Resource	8	8.2	65.6%	●

Rank	Risk ID	Title	Project	Impact	Prob	Exposure	Status
3	RISK-QA-002	E2E Test Coverage Gaps	QA	8.5	7.8	66.3%	
4	RISK-TECH-001	Payment API Issues	Tech	9.5	6.5	61.75%	
5	RISK-SCHED-001	Missed Release Dates	Schedule	8	7.5	60%	
6	RISK-TECH-002	WebView-Native Bridge	Tech	8	7.6	60.8%	
7	RISK-TECH-003	Desktop Sync Deadlock	Tech	8	6.8	54.4%	
8	RISK-QA-003	Regression Test Coverage	QA	7.5	7.2	54%	
9	RISK-RES-002	DevOps Single Point Failure	Resource	8.5	5.8	49.3%	
10	RISK-TECH-004	Browser Compatibility	Tech	6	7.0	42%	
11-30	[20 more]	Medium & Low Priority Risks	Mixed	4-6	3-5	12-35%	

Risk Ownership & Accountability

Risk Owners

Risk Category	Owner	Backup	Escalation
QA/Testing	Rebecca Santos (QA Lead)	Fiona MacDonald	VP QA (TBD)
Resources	Miguel Rodriguez (Tech Lead)	Sarah Chen (PM)	CTO
Schedule	Sarah Chen (PM)	Miguel Rodriguez	VP Product

Risk Category	Owner	Backup	Escalation
Technical	Miguel Rodriguez (Tech Lead)	James Wilson (PM)	CTO
Business	James Wilson (PM)	Sarah Chen	VP Business

Risk Communication Plan

Stakeholder Updates

Stakeholder	Frequency	Format	Detail Level
Executive Steering Committee	Monthly	Dashboard + Report	Executive summary
Development Teams	Daily (Standups)	Verbal + Jira	Detailed, actionable
Department Heads	Bi-weekly	Metrics Review	High-level trends
Project Team	Weekly	Risk Review Meeting	Full analysis
Clients	As needed	Email/Call	Business impact focus

Escalation Procedure

- Level 1 (Yellow Alert):

Risk exposure > 45%

→ Notify Risk Owner & Team Lead
- Level 2 (Orange Alert):

Risk exposure > 60% OR trend worsening

→ Notify VP Engineering + PMO

→ Daily monitoring

→ Consider mitigation budget
- Level 3 (Red Alert):

Risk exposure > 75% OR materialized

→ Escalate to CTO/VP Product

→ Executive steering committee

→ Initiate contingency plans

→ Daily status updates

Historical Risk Tracking

Risk Evolution (Last 8 Weeks)

- Week of April 1:

RISK-QA-001 exposure: 58% (MEDIUM)
- Week of April 8:

RISK-QA-001 exposure: 62% (HIGH)
- Week of April 15:

RISK-QA-001 exposure: 68% (HIGH) ← Escalated
- Week of April 22:

RISK-QA-001 exposure: 71% (CRITICAL)
- Week of April 29:

RISK-QA-001 exposure: 74% (CRITICAL)
- Week of May 3:

RISK-QA-001 exposure: 76.5% (CRITICAL) ← NOW

Trend Analysis:  **ACCELERATING** - Exposure increasing 2-3% weekly

Risks Closed This Quarter

Risk ID	Title	Status	Resolution
RISK-OLD-001	Legacy Database Migration	 CLOSED	Completed early
RISK-OLD-002	Third-party Integration	 CLOSED	Vendor certified

Recommendations

For Executive Leadership

1. **APPROVE IMMEDIATE HIRING** - 3 positions (Backend, QA, Android)
 - Budgetary impact: \$280k/year
 - ROI: Prevents \$500k+ in potential losses
 - Timeline: Posting today, hires by June 1
2. **ALLOCATE QA TESTING BUDGET** - \$50k for automation infrastructure & contractors
 - Implement test automation framework
 - Contract external QA support if needed
 - Reduce defect escape rate to < 5%
3. **REVIEW RELEASE TIMELINE** - Add 2-week contingency buffer
 - E-Commerce: 2026-06-15 → 2026-06-29
 - Provides QA cushion
 - Reduces rushed release risk

For Engineering Leadership

1. **STABILIZE QA TEAM** - Implement immediate support
 - Assign James Wilson (1 day/week) to test execution
 - Borrow contractors for regression testing
 - Reduce Rebecca's context switching
2. **PRIORITIZE TEST AUTOMATION** - Start immediately
 - Week 1: Playwright setup
 - Week 2-3: Implement top 50 regression tests
 - Target: 50% automation coverage by June 30
3. **IMPLEMENT PROCESS IMPROVEMENTS**
 - Test prioritization matrix (Critical-to-Low)
 - Test case management system (replace Google Docs)
 - Daily QA-Dev sync to eliminate blocking

For Project Management

1. **DAILY RISK MONITORING**
 - Track all 5 CRITICAL risks daily
 - Weekly risk review meetings
 - Escalate any trend changes immediately

2.  **SCOPE ADJUSTMENT**
- Reduce E-Commerce Phase 2 features by 15%
 - Extend timeline for WebApp redesign to Q3
 - Focus resources on critical path items
3.  **CONTINGENCY PLANNING**
- Prepare contingency plans A, B, C
 - Brief stakeholders on scenarios
 - Have contractor list ready

Risk Metrics & KPIs

Portfolio-Level Metrics

Metric	Current	Target	Trend
Critical Risks	5	≤ 2	 Increasing
Avg Risk Exposure	49%	< 35%	 Concerning
Risks > 60% Exposure	6	≤ 2	 Worsening
Open Mitigation Actions	23	15	 In Progress
Mitigation Success Rate	72%	> 85%	 Declining

Risk Velocity

New Risks Identified:8/month (↑40% from 5/month in Q1)

Risks Closed/Resolved:2/month (↓60% from 5/month in Q1)

Risk Exposure Trend:+6.2 points/month (↑ ACCELERATING)

Mitigation Plan Adherence: 72% (Target: 90%)

References & Dependencies

Related Documents

- `BUG_TRACKING_TICKETS_2026-05-03.md` - Bug details
- `RESOURCE_ALLOCATION_MATRIX_2026-05-03.md` - Staffing analysis
- `QA_AUDIT_CHECKLIST_2026-05-03.md` - QA procedures
- `TEST_COVERAGE_REPORT_2026-05-03.md` - Current test status

External References

- JIRA Epic: CTI-250 "Quality Assurance Improvement"
- Hiring Requisitions: HR-2024-001, 002, 003
- Budget Allocation: Finance Approval pending

Sign-Off & Approval

Role	Name	Date	Signature
Risk Owner (QA)	Rebecca Santos	2026-05-03	[Pending]
Risk Sponsor (CTO)	[TBD]	-	[Pending]
Executive Approval	[VP Engineering]	-	[Pending]

Distribution

-  **URGENT:** Executive Steering Committee (immediate)
-  **URGENT:** Engineering Leadership (immediate)
-  **PRIORITY:** Development Teams (by end of week)
-  **INFO:** HR & Finance (for hiring/budget)
-  **INFO:** Project Management Office

Document Classification: INTERNAL - Confidential

Next Review Date: 2026-05-10 (Weekly)

Annual Review Date: 2026-05-03, 2026-08-03, 2026-11-03

Risk Report Custodian: Risk Management Office

Questions/Concerns: Contact Rebecca Santos (QA Lead) or Miguel Rodriguez (Tech Lead)

"Proactive risk management prevents reactive crisis management"

— *Risk Management Principle*
